
Gantt Chart Report

Delivering a clear and reliable schedule that keeps every milestone on track.

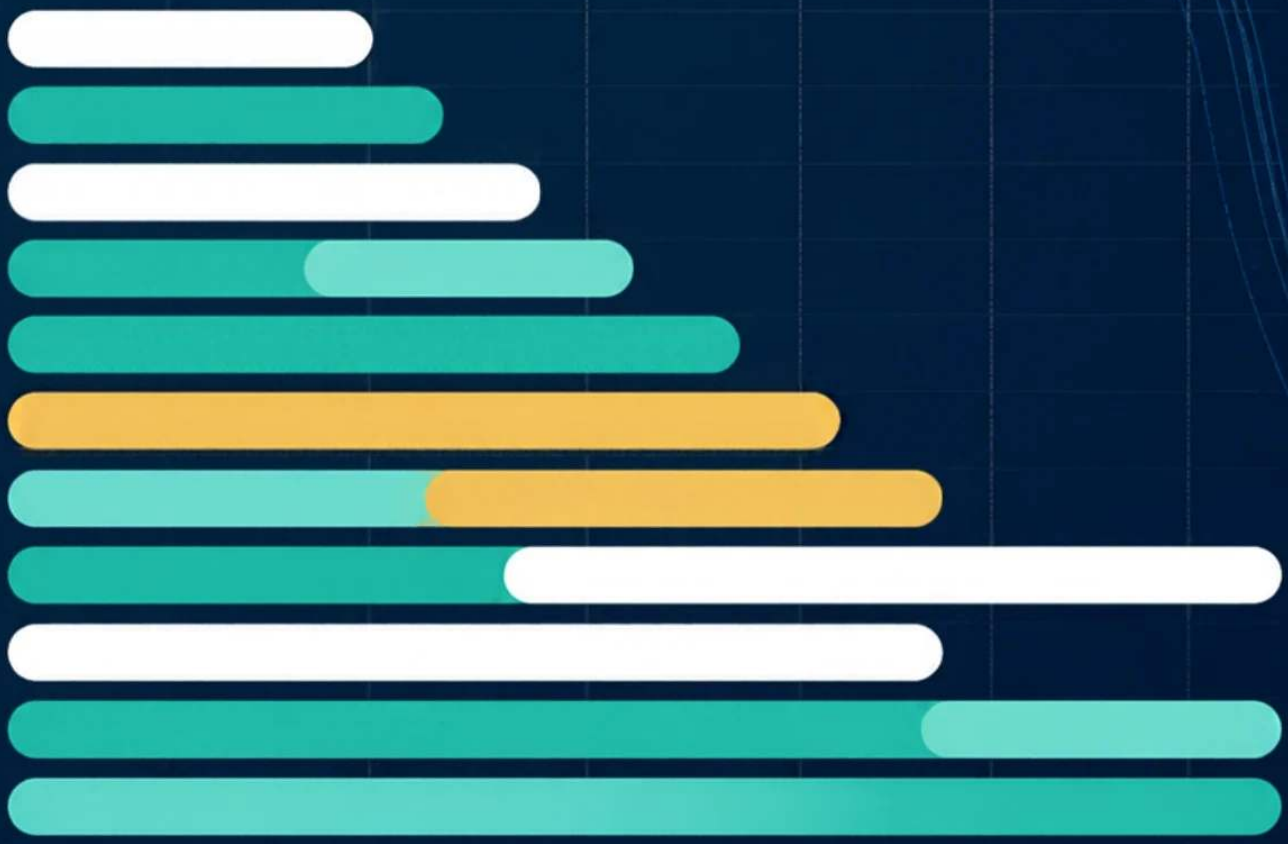

Sample Project

Client: Urban City

PREPARED & SUBMITTED BY

SP Consultant

in Joint Venture with USF Consultants
info@spconsultant.example
shahidpervaiz.net

ISSUE

November 2026

DESIGN & CONSTRUCTION PROGRAMME

Sample Project

Generated: 08 November 2026

CLIENT	PROGRAMME START	PROGRAMME FINISH	STATUS DATE	TOTAL ACTIVITIES
Urban City	17/11/2025	10/02/2027	31/10/2026	54

1. EXECUTIVE SUMMARY

Sample Project is being carried out for Urban City at Sample City under contract C-2026-014. It started on 17 November 2025 and is due for completion on 10 February 2027. This Gantt Chart Report sets out the position at 8 November 2026 and has been prepared by SP Consultant in joint venture with USF Consultants.

This report presents the schedule status for **Sample Project**, prepared for **Urban City**, as of status date **31/10/2026**.

The programme comprises **54** activities, running from **17/11/2025** to **10/02/2027** (**451** days elapsed), at an average completion of **74.8%** (the simple average of the activities' % complete, not weighted by duration or value).

Of these, **37** are complete, **5** on track, **0** at risk, **0** behind the current programme, and **12** not yet started. No activity is behind the current programme at the status date. Delay against the approved baseline is a separate measure, analysed with the Schedule Delay Analysis Tool.

35 activities sit on the critical path (zero float) — any delay to these activities will push back the overall finish date of **10/02/2027** by the same amount.

PROJECT NO.	001	PROJECT	Sample Project
CLIENT	Urban City	LOCATION	Sample City
CONTRACT NO.	C-2026-014	CONSULTANT	SP Consultant in joint venture with USF Consultants
START DATE	17 November 2025	COMPLETION DATE	10 February 2027
REPORT DATE	8 November 2026	STATUS DATE	31 October 2026


2. PROGRESS SUMMARY

TOTAL ACTIVITIES	AVG % COMPLETE	COMPLETED
54	74.8%	37


AT RISK	BEHIND SCHEDULE	NOT STARTED
0	0	12

CRITICAL PATH
35

3. GANTT TIMELINE

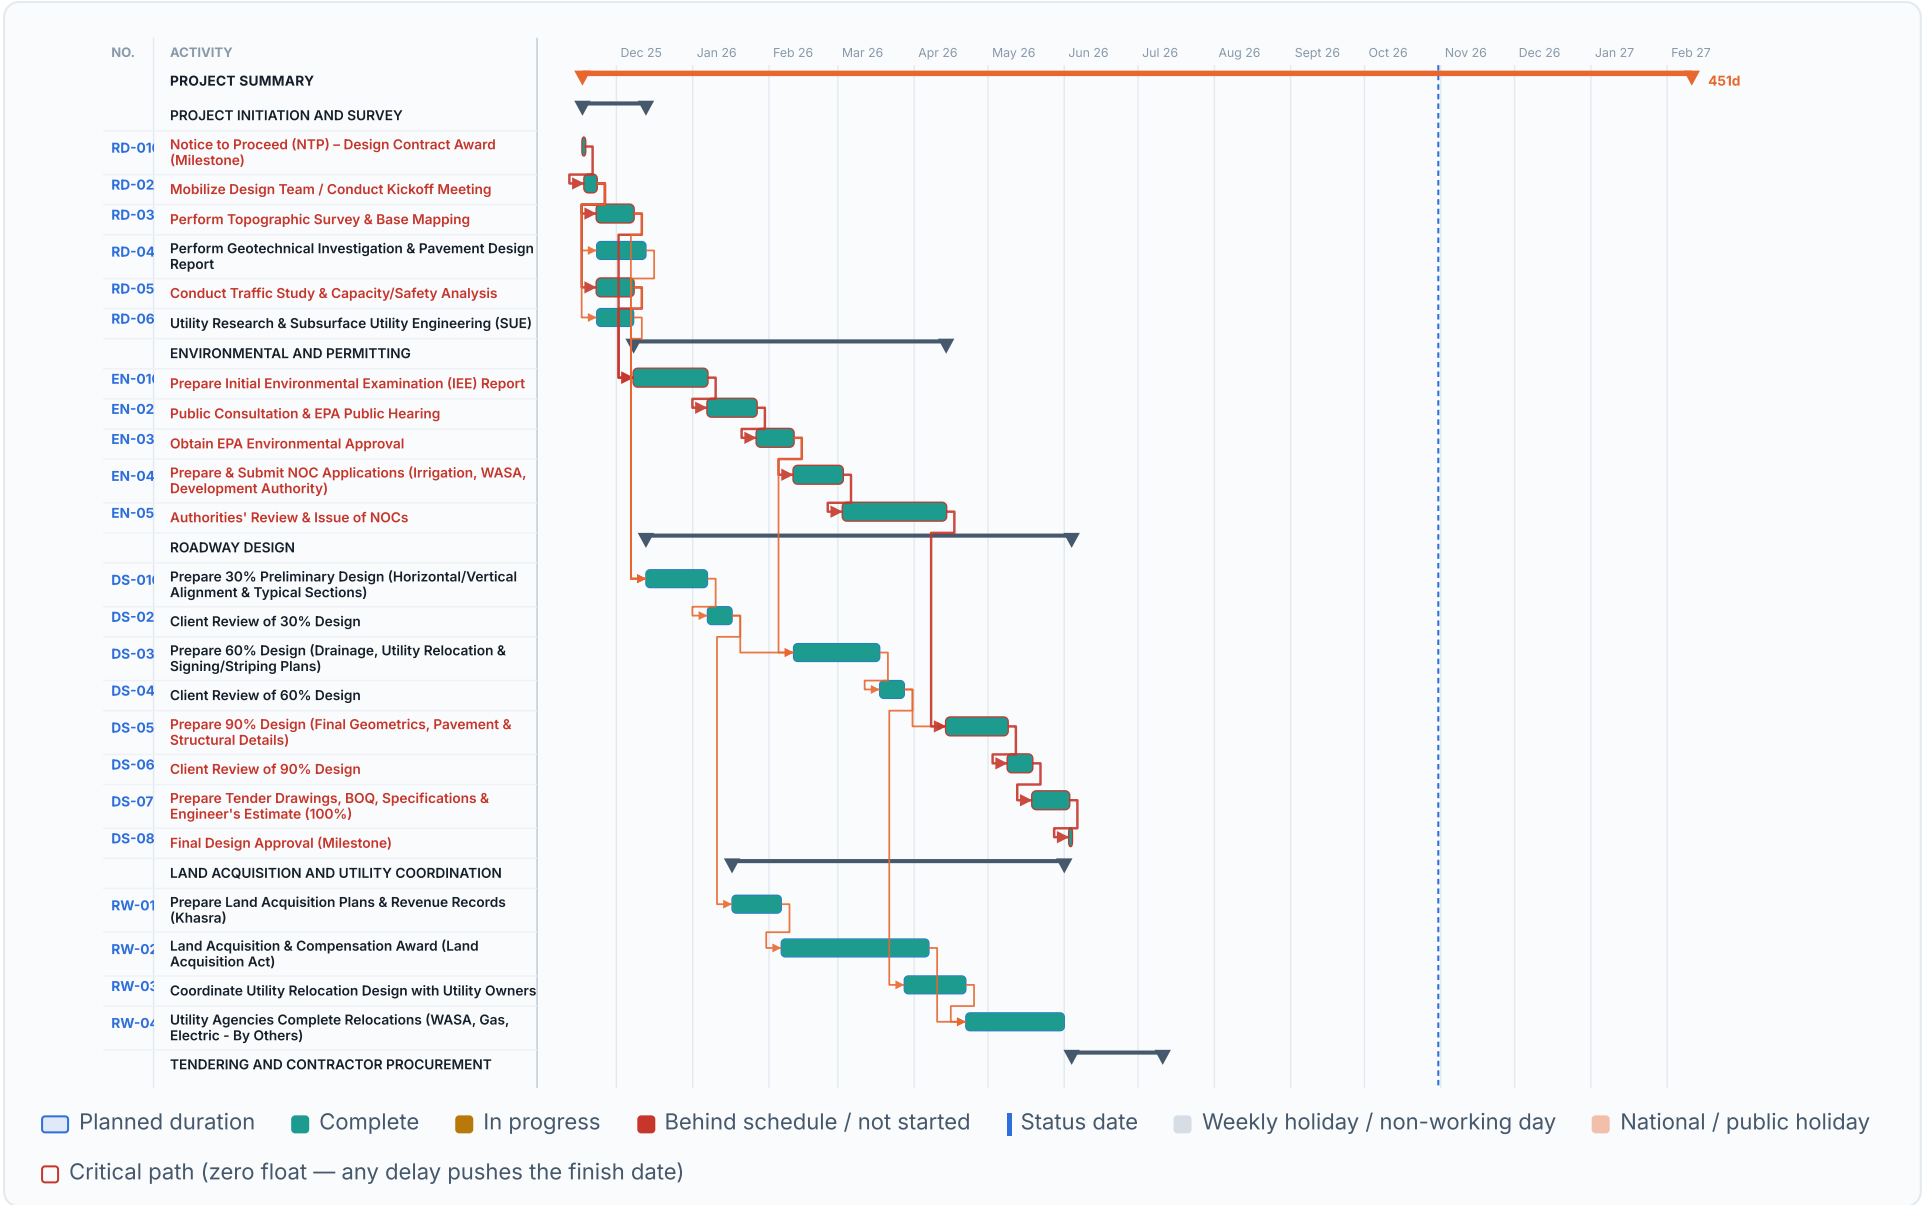

Gantt Timeline (continued, page 2 of 3)

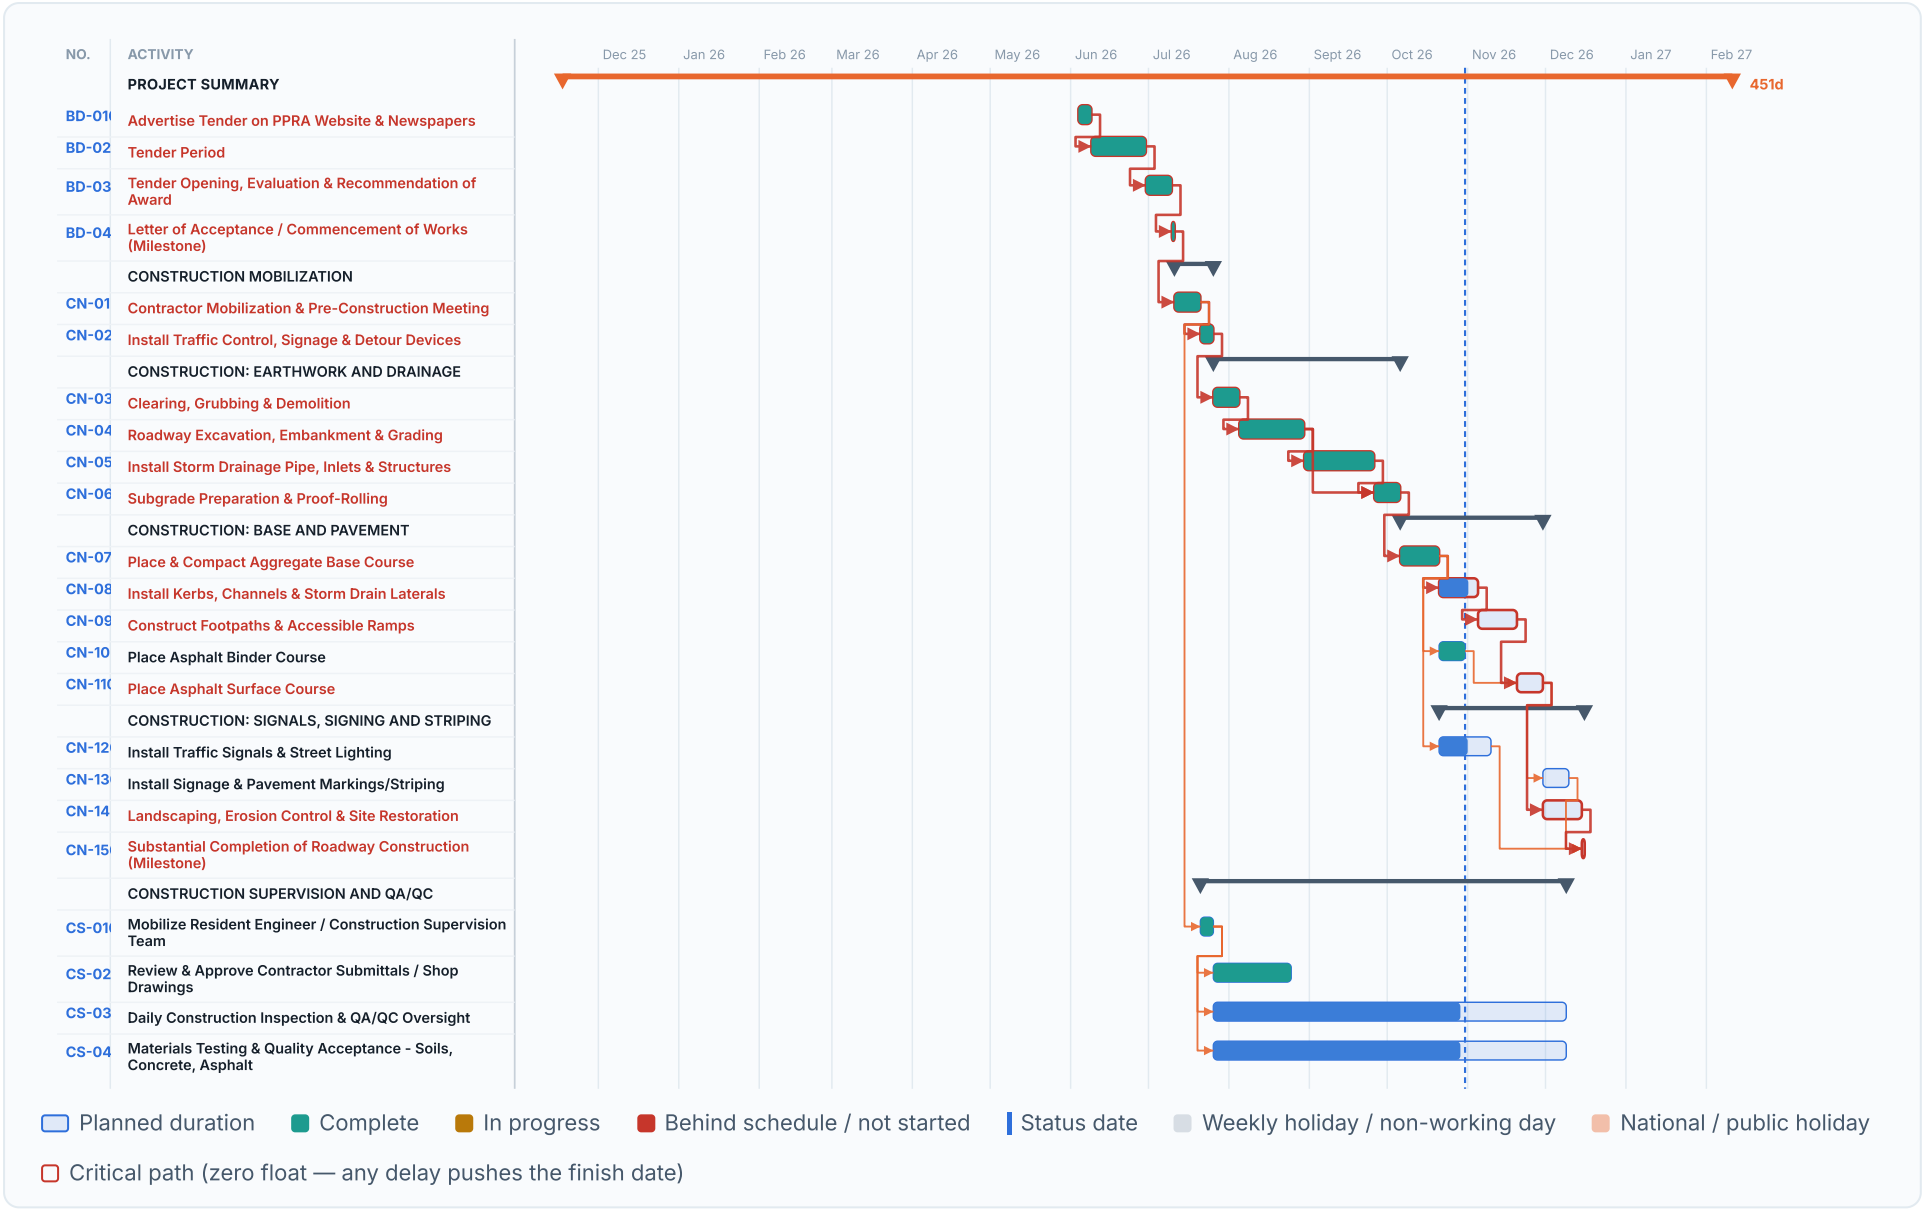

Gantt Timeline (continued, page 3 of 3)



Working Calendar

WORKING DAYS

Mon, Tue, Wed, Thu, Fri, Sat, Sun (7 days a week)

WEEKLY HOLIDAYS

None

DAILY WORKING HOURS

Not specified

NATIONAL / PUBLIC HOLIDAYS

None

Durations are counted in working days: the weekly holidays and national / public holidays above are non-working days and are skipped when dates are calculated. Daily working hours are shown for information only.

4. CRITICAL PATH ACTIVITIES

NO.	ACTIVITY	START	FINISH	DURATION
RD-010	**Notice to Proceed (NTP) – Design Contract Award (Milestone)**	17/11/2025	17/11/2025	1 d
RD-020	**Mobilize Design Team / Conduct Kickoff Meeting**	18/11/2025	22/11/2025	5 d
RD-030	**Perform Topographic Survey & Base Mapping**	23/11/2025	07/12/2025	15 d
RD-050	**Conduct Traffic Study & Capacity/Safety Analysis**	23/11/2025	07/12/2025	15 d
EN-010	**Prepare Initial Environmental Examination (IEE) Report**	08/12/2025	06/01/2026	30 d
EN-020	**Public Consultation & EPA Public Hearing**	07/01/2026	26/01/2026	20 d
EN-030	**Obtain EPA Environmental Approval**	27/01/2026	10/02/2026	15 d
EN-040	**Prepare & Submit NOC Applications (Irrigation, WASA, Development Authority)**	11/02/2026	02/03/2026	20 d
EN-050	**Authorities' Review & Issue of NOCs**	03/03/2026	13/04/2026	42 d
DS-050	**Prepare 90% Design (Final Geometrics, Pavement & Structural Details)**	14/04/2026	08/05/2026	25 d
DS-060	**Client Review of 90% Design**	09/05/2026	18/05/2026	10 d
DS-070	**Prepare Tender Drawings, BOQ, Specifications & Engineer's Estimate (100%)**	19/05/2026	02/06/2026	15 d
DS-080	**Final Design Approval (Milestone)**	03/06/2026	03/06/2026	1 d
BD-010	**Advertise Tender on PPRA Website & Newspapers**	04/06/2026	08/06/2026	5 d
BD-020	**Tender Period**	09/06/2026	29/06/2026	21 d
BD-030	**Tender Opening, Evaluation & Recommendation of Award**	30/06/2026	09/07/2026	10 d
BD-040	**Letter of Acceptance / Commencement of Works (Milestone)**	10/07/2026	10/07/2026	1 d
CN-010	**Contractor Mobilization & Pre-Construction Meeting**	11/07/2026	20/07/2026	10 d
CN-020	**Install Traffic Control, Signage & Detour Devices**	21/07/2026	25/07/2026	5 d
CN-030	**Clearing, Grubbing & Demolition**	26/07/2026	04/08/2026	10 d
CN-040	**Roadway Excavation, Embankment & Grading**	05/08/2026	29/08/2026	25 d
CN-050	**Install Storm Drainage Pipe, Inlets & Structures**	30/08/2026	25/09/2026	27 d
CN-060	**Subgrade Preparation & Proof-Rolling**	26/09/2026	05/10/2026	10 d
CN-070	**Place & Compact Aggregate Base Course**	06/10/2026	20/10/2026	15 d
CN-080	**Install Kerbs, Channels & Storm Drain Laterals**	21/10/2026	04/11/2026	15 d
CN-090	**Construct Footpaths & Accessible Ramps**	05/11/2026	19/11/2026	15 d
CN-110	**Place Asphalt Surface Course**	20/11/2026	29/11/2026	10 d

NO.	ACTIVITY	START	FINISH	DURATION
CN-140	**Landscaping, Erosion Control & Site Restoration**	30/11/2026	14/12/2026	15 d
CN-150	**Substantial Completion of Roadway Construction (Milestone)**	15/12/2026	15/12/2026	1 d
CO-010	**Substantial Completion Inspection & Punch List Walkthrough**	16/12/2026	25/12/2026	10 d
CO-020	**Punch List Corrective Work**	26/12/2026	09/01/2027	15 d
CO-030	**Prepare As-Built / Record Drawings**	10/01/2027	24/01/2027	15 d
CO-040	**Final Inspection & Acceptance (Milestone)**	25/01/2027	25/01/2027	1 d
CO-060	**Submit Final Closeout Documents (Warranties, O&M Manuals, Final Payment Certificate)**	26/01/2027	09/02/2027	15 d
CO-070	**Project Completion (Milestone)**	10/02/2027	10/02/2027	1 d

5. CONSTRAINTS & SCHEDULE RISKS

Date constraints

No date constraints are applied: every linked activity is scheduled purely by its predecessor logic, so the programme dates respond fully to progress and delays.

Schedule issues and implications

WARNING **Very long activities**

3 activities are longer than 44 working days (about two months). Long activities are hard to monitor; consider breaking them into shorter measurable steps.

Activities: CS-030 Daily Construction Inspection & QA/QC Oversight, CS-040 Materials Testing & Quality Acceptance - Soils, Concrete, Asphalt, CS-050 Weekly Progress Meetings & Interim Payment Certificates (IPCs)

WARNING **Little schedule flexibility**

11 of the 17 remaining activities (65%) are critical. With so little float, almost any delay will move the completion date.

NOTE **Near-critical activities**


1 incomplete activity has only 1–5 working days of float. A small delay would make it critical.

Activities: CN-130 Install Signage & Pavement Markings/Striping


6. RESOURCE SUMMARY

No resources have been added to any activity yet — use the 📦 button on an activity row to add Material, Manpower or Equipment.

7. SCHEDULE PROGRESS CHART

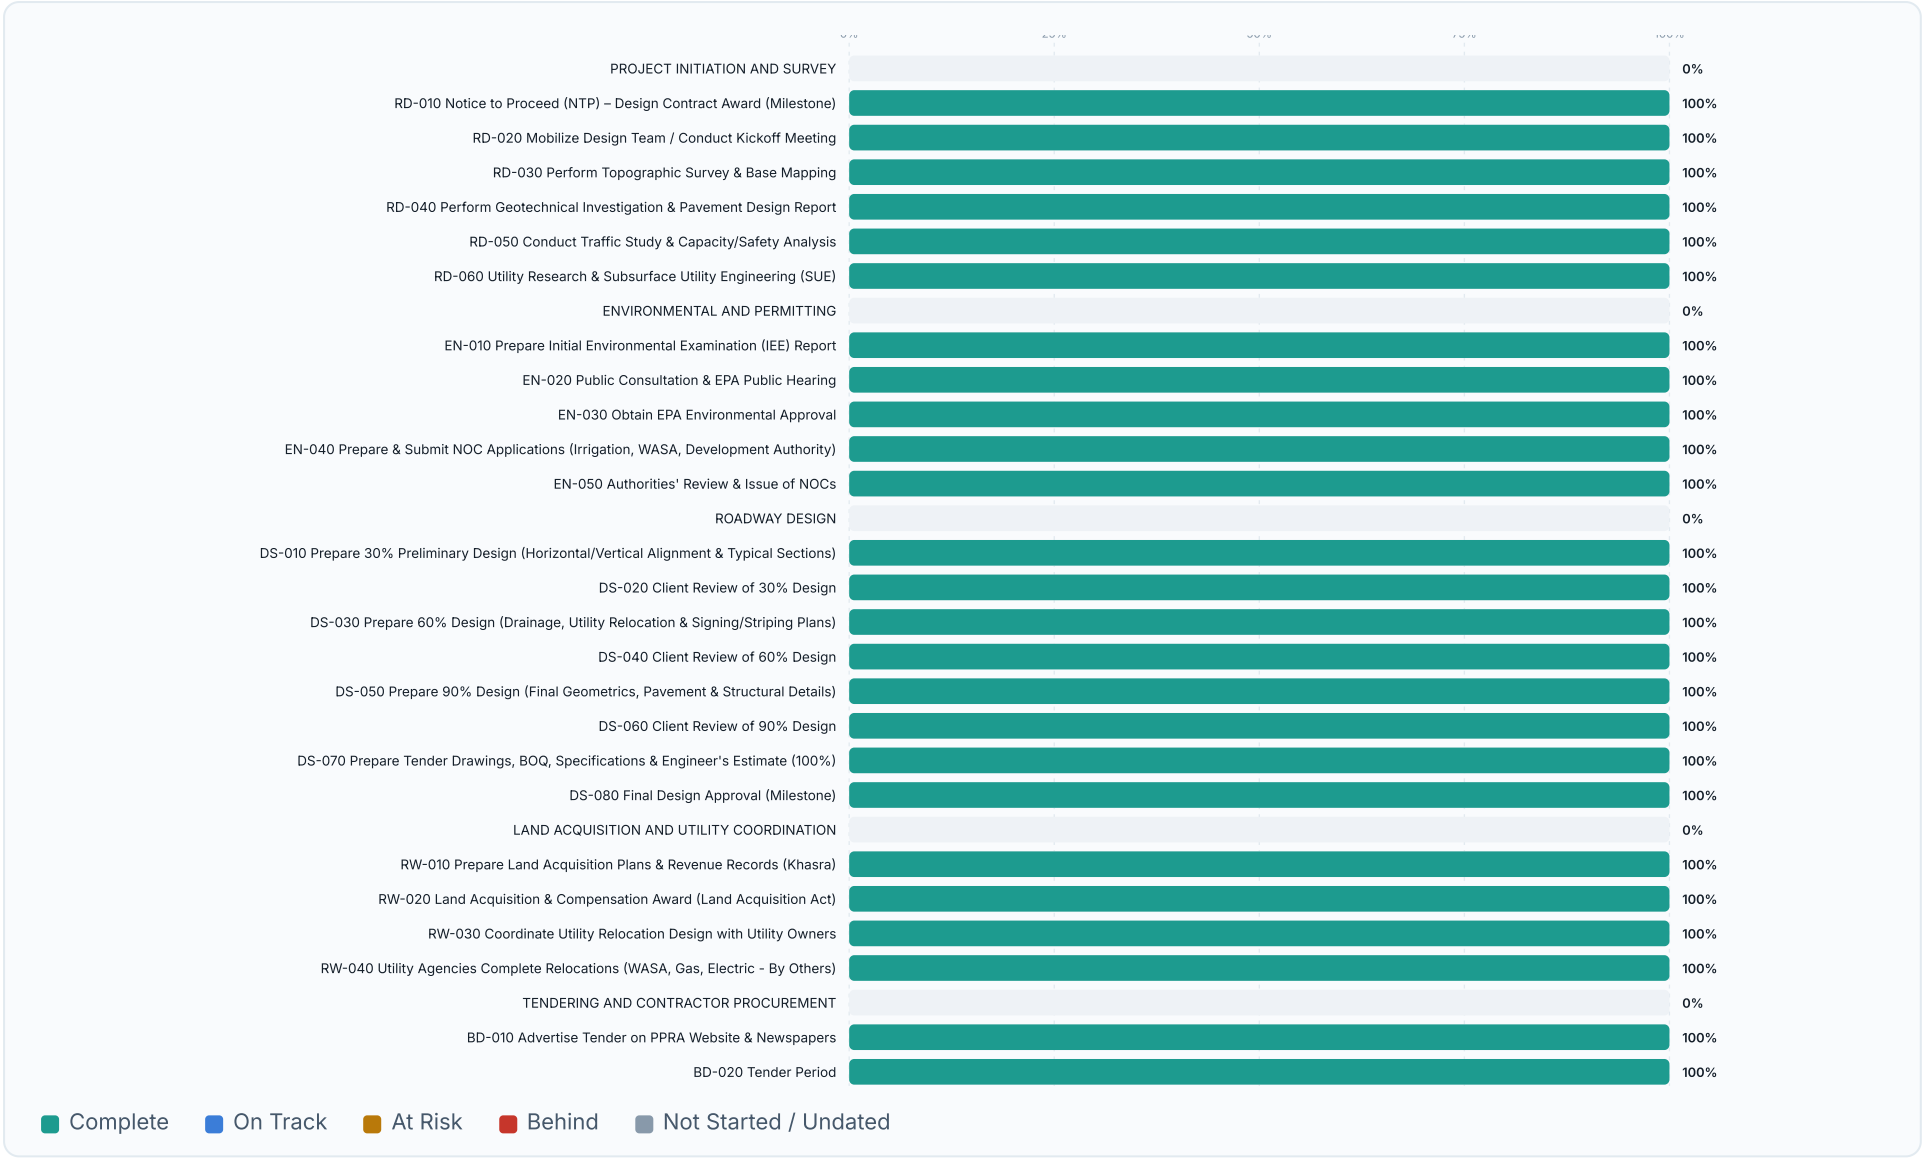

Schedule Progress Chart (continued, page 2 of 3)

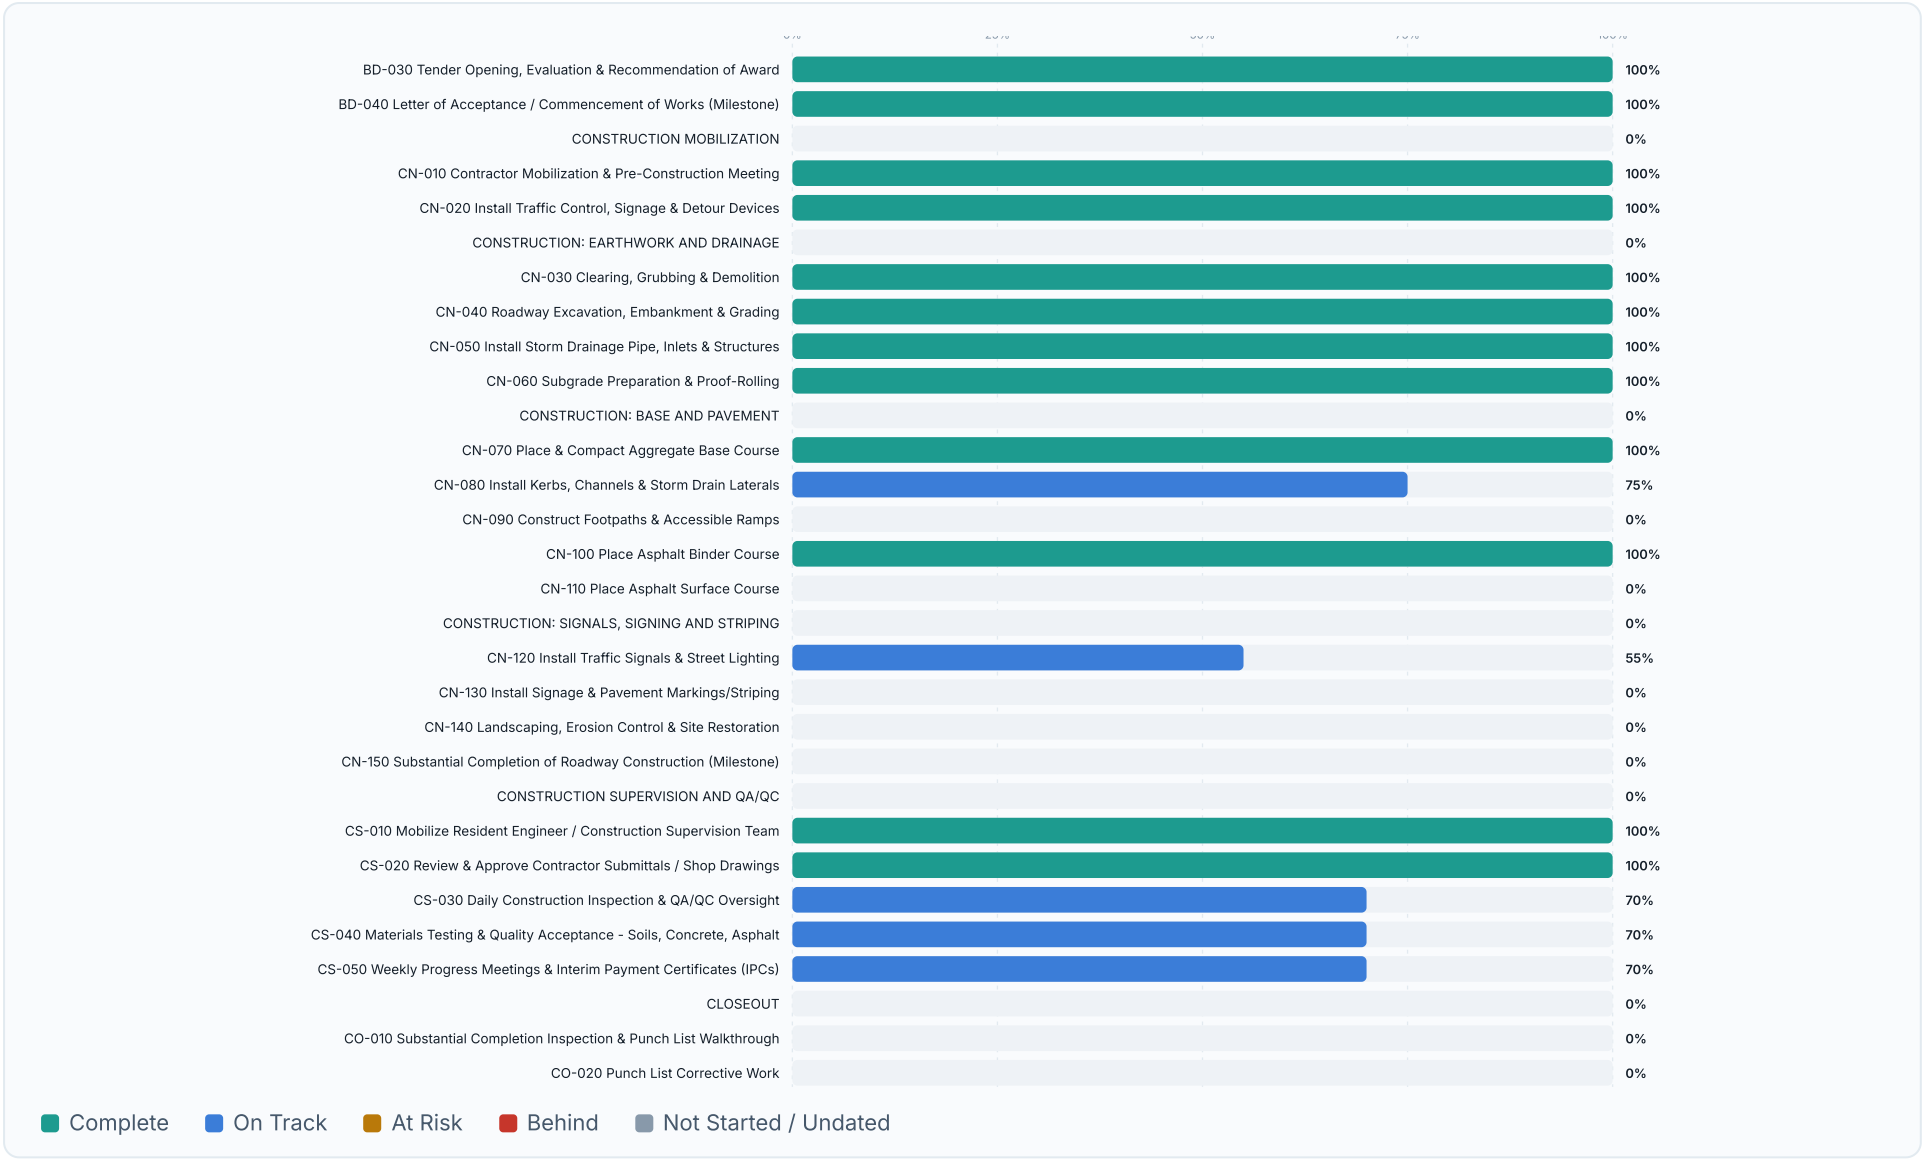

Sample report: illustrative data

Schedule Progress Chart (continued, page 3 of 3)



8. BREAKDOWN

BY STATUS	
Complete	37
Not Started	12
On Track	5

BY WBS SECTION	
Roadway Design	8
Closeout	7
Project Initiation and Survey	6
Environmental and Permitting	5
Construction: Base and Pavement	5
Construction Supervision and QA/QC	5
Land Acquisition and Utility Coordination	4
Tendering and Contractor Procurement	4
Construction: Earthwork and Drainage	4
Construction: Signals, Signing and Striping	4
Construction Mobilization	2

9. FULL ACTIVITY SCHEDULE

NO.	ACTIVITY	START	FINISH	DURATION (WORKING DAYS)	CALENDAR DAYS	FLOAT	% COMPLETE	STATUS
	PROJECT INITIATION AND SURVEY	—	—	—	—	—	0%	Undated
RD-010	**Notice to Proceed (NTP) – Design Contract Award (Milestone)**	17/11/2025	17/11/2025	1 d	1	Critical	100%	Complete
RD-020	**Mobilize Design Team / Conduct Kickoff Meeting**	18/11/2025	22/11/2025	5 d	5	Critical	100%	Complete
RD-030	**Perform Topographic Survey & Base Mapping**	23/11/2025	07/12/2025	15 d	15	Critical	100%	Complete
RD-040	**Perform Geotechnical Investigation & Pavement Design Report**	23/11/2025	12/12/2025	20 d	20	42d	100%	Complete
RD-050	**Conduct Traffic Study & Capacity/Safety Analysis**	23/11/2025	07/12/2025	15 d	15	Critical	100%	Complete
RD-060	**Utility Research & Subsurface Utility Engineering (SUE)**	23/11/2025	07/12/2025	15 d	15	47d	100%	Complete
	ENVIRONMENTAL AND PERMITTING	—	—	—	—	—	0%	Undated
EN-010	**Prepare Initial Environmental Examination (IEE) Report**	08/12/2025	06/01/2026	30 d	30	Critical	100%	Complete
EN-020	**Public Consultation & EPA Public Hearing**	07/01/2026	26/01/2026	20 d	20	Critical	100%	Complete
EN-030	**Obtain EPA Environmental Approval**	27/01/2026	10/02/2026	15 d	15	Critical	100%	Complete
EN-040	**Prepare & Submit NOC Applications (Irrigation, WASA, Development Authority)**	11/02/2026	02/03/2026	20 d	20	Critical	100%	Complete
EN-050	**Authorities' Review & Issue of NOCs**	03/03/2026	13/04/2026	42 d	42	Critical	100%	Complete
	ROADWAY DESIGN	—	—	—	—	—	0%	Undated
DS-010	**Prepare 30% Preliminary Design (Horizontal/Vertical Alignment & Typical Sections)**	13/12/2025	06/01/2026	25 d	25	42d	100%	Complete
DS-020	**Client Review of 30% Design**	07/01/2026	16/01/2026	10 d	10	42d	100%	Complete
DS-030	**Prepare 60% Design (Drainage, Utility Relocation & Signing/Striping Plans)**	11/02/2026	17/03/2026	35 d	35	17d	100%	Complete
DS-040	**Client Review of 60% Design**	18/03/2026	27/03/2026	10 d	10	17d	100%	Complete
DS-050	**Prepare 90% Design (Final Geometrics, Pavement & Structural Details)**	14/04/2026	08/05/2026	25 d	25	Critical	100%	Complete
DS-060	**Client Review of 90% Design**	09/05/2026	18/05/2026	10 d	10	Critical	100%	Complete
DS-070	**Prepare Tender Drawings, BOQ, Specifications & Engineer's Estimate (100%)**	19/05/2026	02/06/2026	15 d	15	Critical	100%	Complete
DS-080	**Final Design Approval (Milestone)**	03/06/2026	03/06/2026	1 d	1	Critical	100%	Complete
	LAND ACQUISITION AND UTILITY COORDINATION	—	—	—	—	—	0%	Undated
RW-010	**Prepare Land Acquisition Plans & Revenue Records (Khasra)**	17/01/2026	05/02/2026	20 d	20	54d	100%	Complete
RW-020	**Land Acquisition & Compensation Award (Land Acquisition Act)**	06/02/2026	06/04/2026	60 d	60	54d	100%	Complete
RW-030	**Coordinate Utility Relocation Design with Utility Owners**	28/03/2026	21/04/2026	25 d	25	39d	100%	Complete

NO.	ACTIVITY	START	FINISH	DURATION (WORKING DAYS)	CALENDAR DAYS	FLOAT	% COMPLETE	STATUS
RW-040	**Utility Agencies Complete Relocations (WASA, Gas, Electric - By Others)**	22/04/2026	31/05/2026	40 d	40	39d	100%	Complete
	TENDERING AND CONTRACTOR PROCUREMENT	—	—	—	—	—	0%	Undated
BD-010	**Advertise Tender on PPRA Website & Newspapers**	04/06/2026	08/06/2026	5 d	5	Critical	100%	Complete
BD-020	**Tender Period**	09/06/2026	29/06/2026	21 d	21	Critical	100%	Complete
BD-030	**Tender Opening, Evaluation & Recommendation of Award**	30/06/2026	09/07/2026	10 d	10	Critical	100%	Complete
BD-040	**Letter of Acceptance / Commencement of Works (Milestone)**	10/07/2026	10/07/2026	1 d	1	Critical	100%	Complete
	CONSTRUCTION MOBILIZATION	—	—	—	—	—	0%	Undated
CN-010	**Contractor Mobilization & Pre-Construction Meeting**	11/07/2026	20/07/2026	10 d	10	Critical	100%	Complete
CN-020	**Install Traffic Control, Signage & Detour Devices**	21/07/2026	25/07/2026	5 d	5	Critical	100%	Complete
	CONSTRUCTION: EARTHWORK AND DRAINAGE	—	—	—	—	—	0%	Undated
CN-030	**Clearing, Grubbing & Demolition**	26/07/2026	04/08/2026	10 d	10	Critical	100%	Complete
CN-040	**Roadway Excavation, Embankment & Grading**	05/08/2026	29/08/2026	25 d	25	Critical	100%	Complete
CN-050	**Install Storm Drainage Pipe, Inlets & Structures**	30/08/2026	25/09/2026	27 d	27	Critical	100%	Complete
CN-060	**Subgrade Preparation & Proof-Rolling**	26/09/2026	05/10/2026	10 d	10	Critical	100%	Complete
	CONSTRUCTION: BASE AND PAVEMENT	—	—	—	—	—	0%	Undated
CN-070	**Place & Compact Aggregate Base Course**	06/10/2026	20/10/2026	15 d	15	Critical	100%	Complete
CN-080	**Install Kerbs, Channels & Storm Drain Laterals**	21/10/2026	04/11/2026	15 d	15	Critical	75%	On Track
CN-090	**Construct Footpaths & Accessible Ramps**	05/11/2026	19/11/2026	15 d	15	Critical	0%	Not Started
CN-100	**Place Asphalt Binder Course**	21/10/2026	30/10/2026	10 d	10	20d	100%	Complete
CN-110	**Place Asphalt Surface Course**	20/11/2026	29/11/2026	10 d	10	Critical	0%	Not Started
	CONSTRUCTION: SIGNALS, SIGNING AND STRIPING	—	—	—	—	—	0%	Undated
CN-120	**Install Traffic Signals & Street Lighting**	21/10/2026	09/11/2026	20 d	20	35d	55%	On Track
CN-130	**Install Signage & Pavement Markings/Striping**	30/11/2026	09/12/2026	10 d	10	5d	0%	Not Started
CN-140	**Landscaping, Erosion Control & Site Restoration**	30/11/2026	14/12/2026	15 d	15	Critical	0%	Not Started
CN-150	**Substantial Completion of Roadway Construction (Milestone)**	15/12/2026	15/12/2026	1 d	1	Critical	0%	Not Started
	CONSTRUCTION SUPERVISION AND QA/QC	—	—	—	—	—	0%	Undated
CS-010	**Mobilize Resident Engineer / Construction Supervision Team**	21/07/2026	25/07/2026	5 d	5	7d	100%	Complete
CS-020	**Review & Approve Contractor Submittals / Shop Drawings**	26/07/2026	24/08/2026	30 d	30	113d	100%	Complete

NO.	ACTIVITY	START	FINISH	DURATION (WORKING DAYS)	CALENDAR DAYS	FLOAT	% COMPLETE	STATUS
CS-030	**Daily Construction Inspection & QA/QC Oversight**	26/07/2026	08/12/2026	136 d	136	7d	70%	On Track
CS-040	**Materials Testing & Quality Acceptance - Soils, Concrete, Asphalt**	26/07/2026	08/12/2026	136 d	136	7d	70%	On Track
CS-050	**Weekly Progress Meetings & Interim Payment Certificates (IPCs)**	26/07/2026	08/12/2026	136 d	136	7d	70%	On Track
	CLOSEOUT	—	—	—	—	—	0%	Undated
CO-010	**Substantial Completion Inspection & Punch List Walkthrough**	16/12/2026	25/12/2026	10 d	10	**Critical**	0%	Not Started
CO-020	**Punch List Corrective Work**	26/12/2026	09/01/2027	15 d	15	**Critical**	0%	Not Started
CO-030	**Prepare As-Built / Record Drawings**	10/01/2027	24/01/2027	15 d	15	**Critical**	0%	Not Started
CO-040	**Final Inspection & Acceptance (Milestone)**	25/01/2027	25/01/2027	1 d	1	**Critical**	0%	Not Started
CO-050	**Contractor Demobilization**	26/01/2027	30/01/2027	5 d	5	10d	0%	Not Started
CO-060	**Submit Final Closeout Documents (Warranties, O&M Manuals, Final Payment Certificate)**	26/01/2027	09/02/2027	15 d	15	**Critical**	0%	Not Started
CO-070	**Project Completion (Milestone)**	10/02/2027	10/02/2027	1 d	1	**Critical**	0%	Not Started

Sample report: illustrative data
