
Safety & HSE Report

Every hazard reported, every incident investigated, everyone home safe.

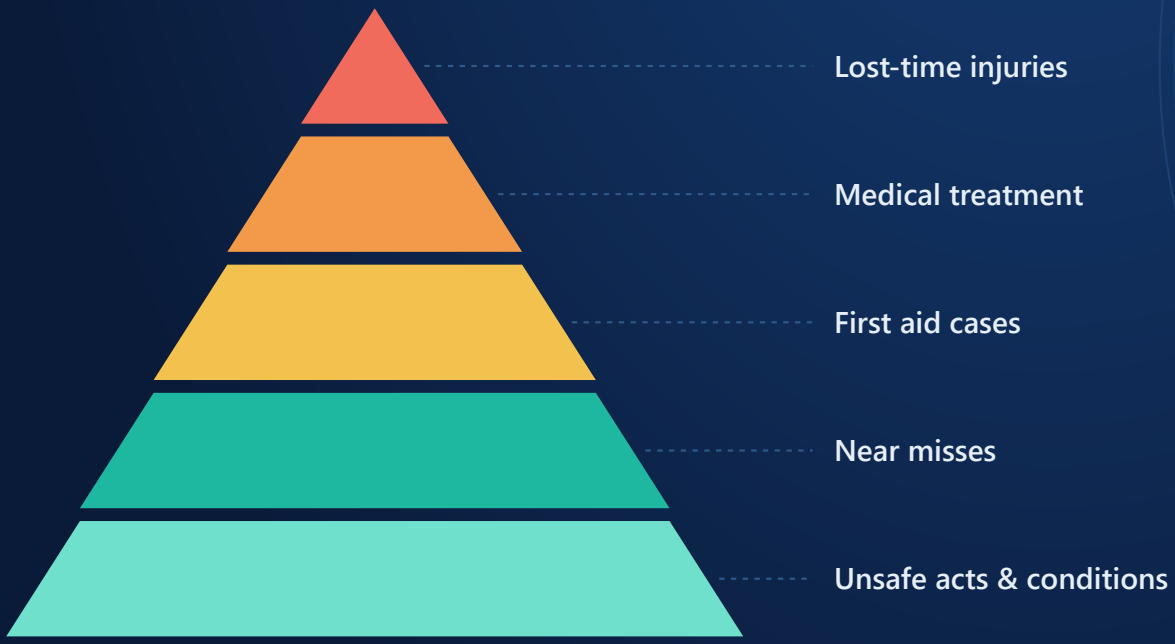

Sample Project

Client: Urban City

PREPARED & SUBMITTED BY

SP Consultant

in Joint Venture with USF Consultants

info@spconsultant.example

shahidpervaiz.net

ISSUE

November 2026

Safety / HSE Report

Sample Project · Urban City · Report date 2026-11-08 · Prepared by H. Safety

TOTAL EVENTS	INCIDENTS	NEAR MISSES	LOST TIME INJURIES	INSPECTIONS
11	2	3	1	1

TOOLBOX TALKS	OPEN CORRECTIVE ACTIONS	LTIFR (PER 1M MAN-HRS)
1	1	6.42

PROJECT INTRODUCTION

PROJECT NO.	001	PROJECT	Sample Project
CLIENT	Urban City	LOCATION	Sample City
CONTRACT NO.	C-2026-014	CONSULTANT	SP Consultant in joint venture with USF Consultants
START DATE	17 November 2025	COMPLETION DATE	22 January 2027
REPORT DATE	8 November 2026	STATUS DATE	8 November 2026

Sample Project is being carried out for Urban City at Sample City under contract C-2026-014. It started on 17 November 2025 and is due for completion on 22 January 2027. This Safety & HSE Report sets out the position at 8 November 2026 and has been prepared by SP Consultant in joint venture with USF Consultants.

HSE Breakdown

BY CATEGORY

Incident	2
Near Miss	3
Lost Time Injury (LTI)	1
Inspection	1
Observation	3
Toolbox Talk	1

CORRECTIVE ACTIONS BY STATUS

Closed	5
Overdue	1

HSE Event Details

Event 1 NEAR MISS LOW CLOSED

DESCRIPTION

Excavator swung close to a worker without a banksman

LOCATION	PERSON INVOLVED	DATE / DAYS LOST
Ch 0+300	Main Contractor LLC crew	2026-07-29

SCANNED COPY

—

REMARKS

HSE-001

Event 2 INCIDENT LOW CLOSED

DESCRIPTION

Worker cut hand on reinforcement bar

LOCATION	PERSON INVOLVED	DATE / DAYS LOST
Ch 0+900	Main Contractor LLC crew	2026-08-14

SCANNED COPY

—

REMARKS

HSE-002

Event 3 OBSERVATION MEDIUM CLOSED

DESCRIPTION

Traffic barriers and night lights missing at the diversion

LOCATION	PERSON INVOLVED	DATE / DAYS LOST
Site entrance Ch 0+000	Main Contractor LLC crew	2026-08-20

SCANNED COPY

—

REMARKS

HSE-003

Event 4 NEAR MISS HIGH CLOSED

DESCRIPTION

Excavator struck an unmarked water main; area evacuated, no injury

LOCATION	PERSON INVOLVED	DATE / DAYS LOST
Ch 1+450	Main Contractor LLC crew	2026-09-08

SCANNED COPY

—

REMARKS

HSE-004

Event 5 INCIDENT MEDIUM CLOSED

DESCRIPTION

Worker slipped into a drainage trench after rain; ankle sprain

LOCATION	PERSON INVOLVED	DATE / DAYS LOST
Ch 1+800	Main Contractor LLC crew	2026-09-17

SCANNED COPY

—

REMARKS

HSE-005

Event 6 OBSERVATION LOW CLOSED

DESCRIPTION

Roller operator without seat belt

LOCATION	PERSON INVOLVED	DATE / DAYS LOST
Ch 2+200	Main Contractor LLC crew	2026-10-03

SCANNED COPY

—

REMARKS

HSE-006

Event 7 TOOLBOX TALK N/A CLOSED

DESCRIPTION

Working next to live traffic and reversing vehicles

LOCATION	PERSON INVOLVED	DATE / DAYS LOST
Site-wide	All crew	2026-10-05

SCANNED COPY

—

REMARKS

HSE-010

Event 8 LOST TIME INJURY (LTI) HIGH CLOSED

DESCRIPTION

Burn to the forearm from hot asphalt during paver cleaning

LOCATION	PERSON INVOLVED	DATE / DAYS LOST
Asphalt paver, Ch 2+050	Main Contractor LLC crew	2026-10-16 · 3 day(s)

SCANNED COPY

—

REMARKS

HSE-007

Event 9 INSPECTION N/A CLOSED

DESCRIPTION

Monthly HSE inspection of the traffic management and plant

LOCATION	PERSON INVOLVED	DATE / DAYS LOST
Ch 0+000 - 3+000	All crew	2026-10-20

SCANNED COPY

—

REMARKS

HSE-011

Event 10 NEAR MISS HIGH UNDER INVESTIGATION

DESCRIPTION

Car entered the work zone at night through a gap in the barriers

LOCATION	PERSON INVOLVED	DATE / DAYS LOST
Ch 2+600	Main Contractor LLC crew	2026-10-24

SCANNED COPY

—

REMARKS

HSE-008

Event 11 OBSERVATION MEDIUM OPEN

DESCRIPTION

Dust above the permit limit during a dry, windy day

LOCATION	PERSON INVOLVED	DATE / DAYS LOST
Asphalt plant	Main Contractor LLC crew	2026-10-28

SCANNED COPY

—

REMARKS

HSE-009

Corrective Action Details

CA-001 CLOSED LINKED TO EVENT 1

ACTION DESCRIPTION

Banksman for every excavator working near people

RESPONSIBLE	TARGET DATE	COMPLETION DATE
S. Agent	2026-07-30	2026-07-30

REMARKS

Briefed at the toolbox talk

CA-002 CLOSED LINKED TO EVENT 4

ACTION DESCRIPTION

Trial pits before excavating within 3 m of any service

RESPONSIBLE	TARGET DATE	COMPLETION DATE
S. Agent	2026-09-10	2026-09-10

REMARKS

Added to the excavation permit

CA-003 CLOSED LINKED TO EVENT 5

ACTION DESCRIPTION

Edge protection and ladders at every open trench

RESPONSIBLE	TARGET DATE	COMPLETION DATE
S. Agent	2026-09-20	2026-09-19

REMARKS

— not yet recorded —

CA-004 CLOSED LINKED TO EVENT 8

ACTION DESCRIPTION

Heat-resistant gloves and sleeves for the paver crew; cleaning procedure revised

RESPONSIBLE	TARGET DATE	COMPLETION DATE
R. Builder	2026-10-20	2026-10-19

REMARKS

Investigation report issued

CA-005 CLOSED LINKED TO EVENT 10

ACTION DESCRIPTION

Close barrier gaps; night inspection logged daily

RESPONSIBLE	TARGET DATE	COMPLETION DATE
S. Agent	2026-10-25	2026-10-25

REMARKS

See ACT-005

CA-006 OVERDUE LINKED TO EVENT 11

ACTION DESCRIPTION

Water sprinkling and dust screens at the asphalt plant

RESPONSIBLE	TARGET DATE	COMPLETION DATE
R. Builder	2026-10-30	—

REMARKS

Overdue: screens not installed
